

One-month timeline and task split for a team of three

Goal for this month: a Flutter app with the 8 screens from the mockup, running on a phone, with **hardcoded data** (no login, backend or real AI yet). Period: **Monday October 5 – Friday October 30, 2026**, 20 working days.

Roles

Erwin

Lead & foundation

- Project setup, theme, shared components
- Tab bar & navigation
- Home, Profile
- Integration & APK build

Teresa

Data & charts

- Data models & dummy data file
- All chart widgets
- Analytics, Food, Scan Meal
- In-memory data across screens

Fadhil

Interaction & animation

- Animation widgets & mascot
- AI Coach (template answers)
- Stress Check, Log Exercise
- Animation polish & device testing

Why this split

- **Split by screen, not by layer.** Each person owns their screens from layout to interaction, so people rarely wait on each other and it is always clear who is working on what.
- **Balanced workload.** Erwin owns the foundation everyone builds on, so he has fewer screens. Teresa owns the charts (the most calculation). Fadhil owns the screens with the most interaction and animation.
- **Two things must be done by day 2:** the theme & base components (Erwin) and the dummy data file (Teresa). The other two people depend on both.


Milestones

Code	Date	What must be demoable
M1	Fri Oct 9	App runs on a phone: correct theme & font, 5-tab bar is clickable, base components ready to use.
M2	Fri Oct 16	Home, Analytics and AI Coach are complete with dummy data.
M3	Fri Oct 23	All 8 screens are complete and every navigation button is connected.
M4	Fri Oct 30	APK ready to share. Logged data (exercise, stress, food) updates Home and Analytics while the app is open.

Note: the existing 8-screen Flutter prototype is already in the repo as a visual and code reference. Starting from it makes weeks 1–2 much faster; use the time saved for clean-up and testing.

Daily timeline

Each box = 1 working day. Thick line = end of week. ◆ = milestone (Friday demo).

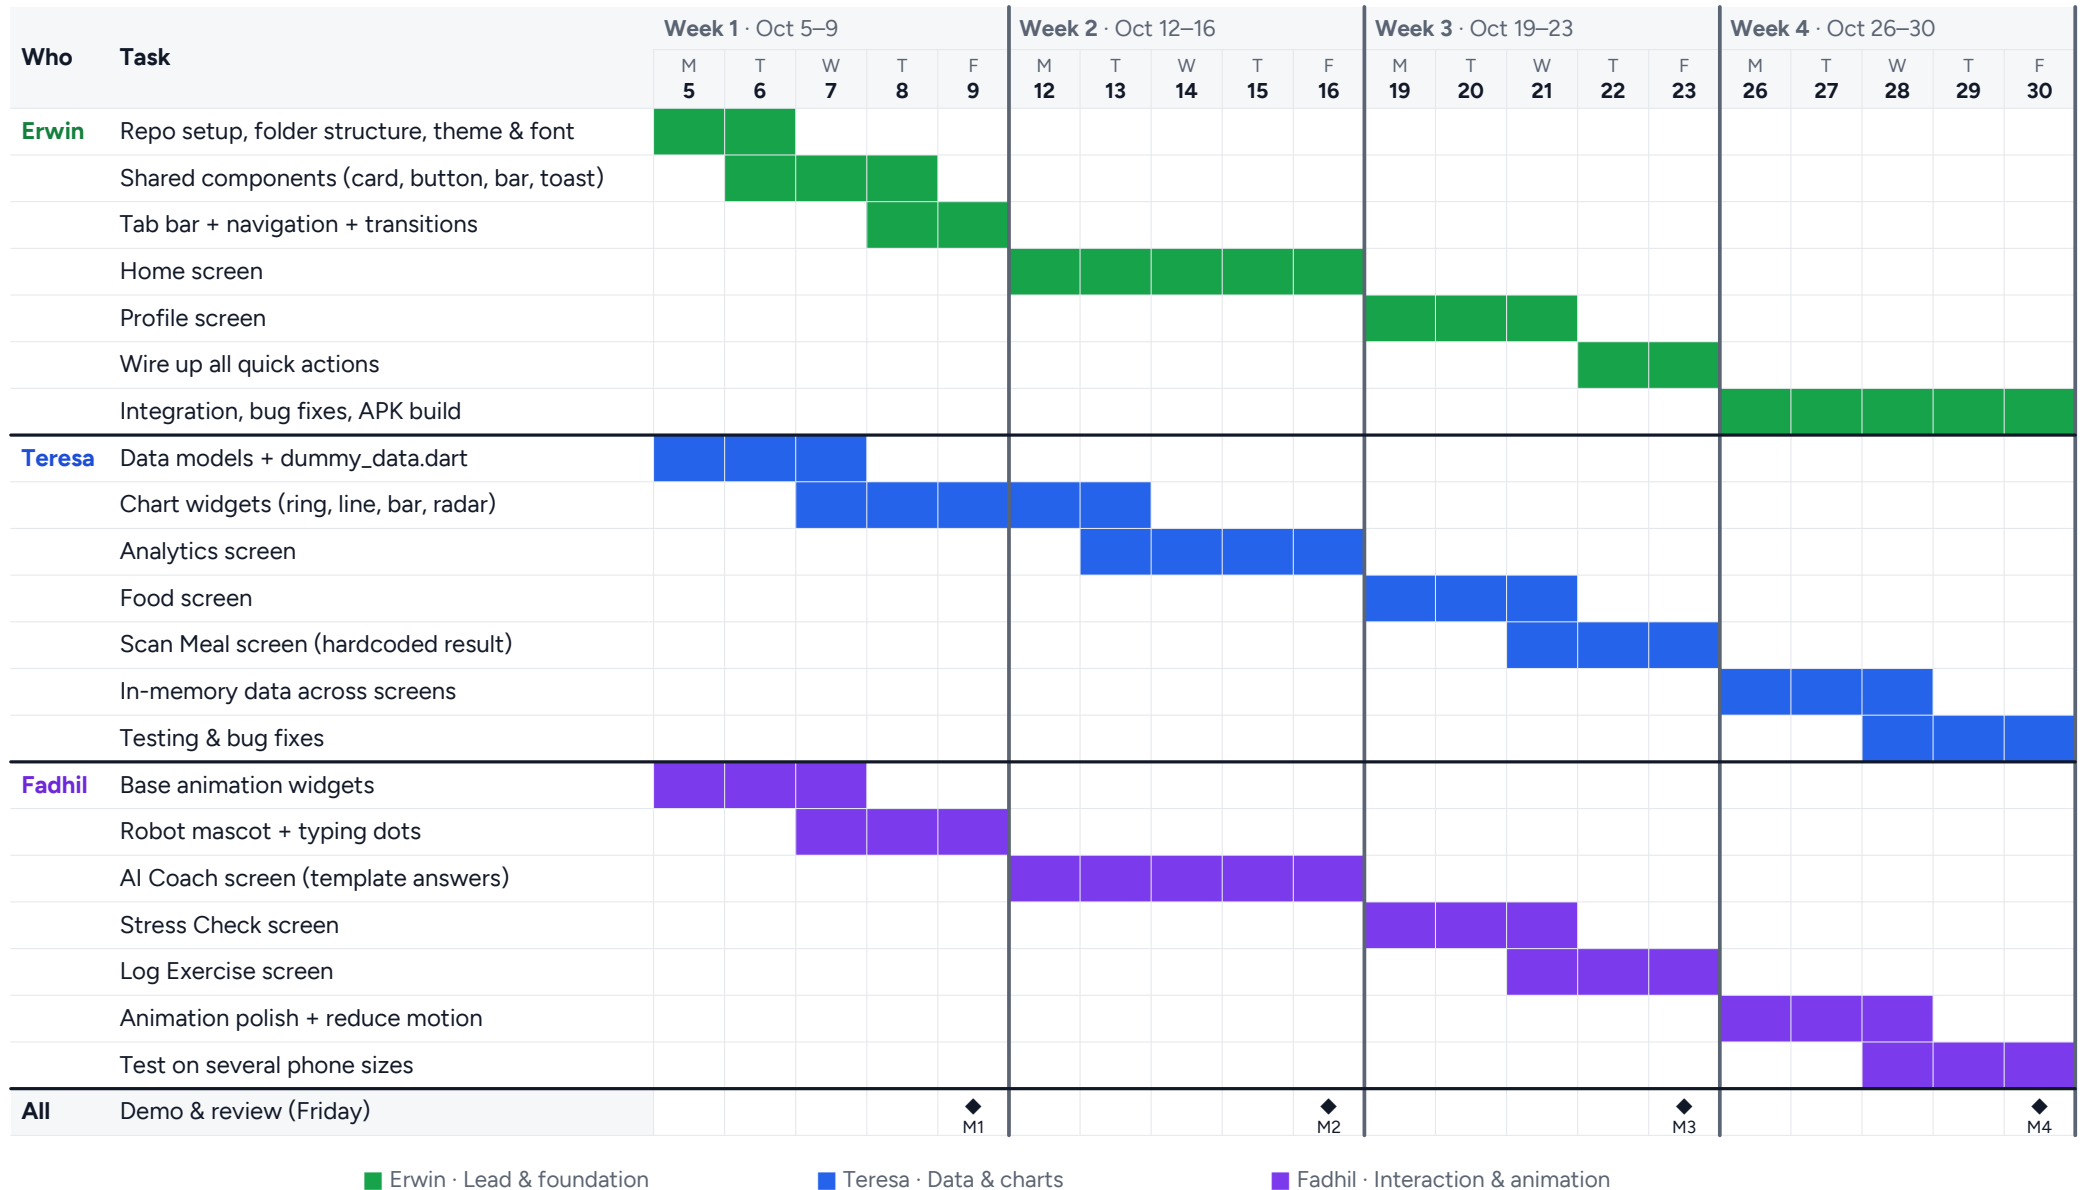

Tasks by week

"Done when" = the condition for a task to count as finished. Estimates are in working days.

Week 1 · Oct 5–9 — Foundation

Who	Task	Days	Done when
Erwin	Create Git repo, Flutter project, folder structure (screens/, widgets/, data/, theme.dart)	1	Everyone can clone and run the app on their own phone.
Erwin	Theme: colors, Figtree font, text styles, motion curves	1	Colors & font match the mockup; used through AppColors and ts().
Erwin	Shared components: AppCard, buttons, ProgressBar, toast, back header	2	Reused on every screen, with examples on a test page.
Erwin	5-tab bar + tab switching + push transition	1	Tabs switch with a 220 ms crossfade; pushed screens slide in from the right.
Teresa	Data models: User, Goal, HealthScore, Meal, Exercise, StressLog, ChatMessage	1	Simple Dart classes, no backend.
Teresa	dummy_data.dart with all sample numbers from the mockup	1	No numbers are hardcoded in screens; everything comes from this file.
Teresa	Chart widgets: score ring, line, bar, radar	3	Take data as input, animate on appear, not clipped on a 360 px phone.
Fadhil	Base animation widgets: FadeUp (staggered entrance), PressScale (press effect)	2	Used in Erwin's components; switch off automatically when "reduce motion" is on.
Fadhil	Robot mascot (floating & blinking) + "typing" dots	2	Looping animations without making the phone hot or laggy.

Week 2 · Oct 12–16 — Core screens

Who	Task	Days	Done when
Erwin	Home: greeting, Health Score card, daily goals, quick log, AI Coach tip	5	Matches the mockup; +250 ml increases water; quick log opens the right screens.
Teresa	Analytics: score trend, Balance (radar), Nutrition, Stress, Exercise, AI Insights, Trends	4	All charts use dummy data; the week picker shows (it may not change data yet).
Fadhil	AI Coach: mascot card, today summary, 4 quick questions, chat, input field	5	Tapping a question shows the message, typing dots, then a template answer; the "not medical advice" note is visible.

Week 3 · Oct 19–23 — All screens

Who	Task	Days	Done when
Erwin	Profile: personal info, daily goals, connected data, settings toggles	3	Toggles switch on and off; other buttons show a "coming soon" toast.
Erwin	Wire up all quick actions on Home, AI Coach and Food	2	No button does nothing when tapped.
Teresa	Food: calorie ring, macros, Scan Meal button, meal list, add meal	3	Total calories are calculated from the meal list in dummy data.
Teresa	Scan Meal: Photo/Barcode/Search modes, scan line, result bottom sheet	3	Scan result is a fixed sample; Search mode can pick from a popular foods list.
Fadhil	Stress Check: 1–10 scale, changing face, factor chips, breathing exercise	3	Breathing circle 4 s in / 4 s out; Save returns to the previous screen + toast.
Fadhil	Log Exercise: activity type, duration, intensity, calorie estimate	3	Calories update when options change; Save returns + toast.

Week 4 · Oct 26–30 — Integration & release

Who	Task	Days	Done when
Erwin	Merge all branches, fix bugs, clean up code	3	No errors in flutter analyze; no screen overflows.
Erwin	Release APK build, app icon & name, install README	2	The APK installs on Android phones other than the developers' own.
Teresa	In-memory state: Log Exercise / Stress / Food results update Home & Analytics	3	Numbers update while the app is open (resetting on close is expected in the hardcoded version).
Teresa	Test all screens & fix own bugs	2	All bugs from the M3 demo are closed.
Fadhil	Polish animations per the Animation Flow board + reduce motion support	3	Durations & curves match the spec table.
Fadhil	Test on 3 phone sizes (small 360 px, medium, large) + log bugs	2	No clipped text; touch targets at least 44 px.

How the team works

- **Git:** one branch per feature (e.g. feature/home). Merge into main through a pull request reviewed by at least one other person.
- **Stand-up:** 15 minutes every morning (what I did yesterday, what I will do today, any blockers). Demo every Friday afternoon.
- **Design reference:** the mockup canvas and the Animation Flow board. When unsure, follow the mockup; write down design changes before building them.
- **Hardcode rule:** all sample data lives only in lib/data/dummy_data.dart. Screens never contain numbers directly. When we move to a backend, only this file changes.
- **Task board:** GitHub Projects with To do / In progress / Review / Done columns.

Folder structure

```
lib/  
  main.dart · theme.dart  
  data/    models.dart, dummy_data.dart (Teresa)  
  widgets/ common.dart (Erwin), charts.dart (Teresa), animated.dart (Fadhil)  
  screens/ home, profile (Erwin) · analytics, food, scan_meal (Teresa) · ai_coach, stress_check, log_exercise  
          (Fadhil)
```

Risks and mitigations

Risk	Mitigation
Theme or dummy data is late, blocking the other two.	Make them the priority for days 1–2. Meanwhile Fadhil can build the mascot and animations, which do not depend on data.
Team members are new to Flutter.	Use the prototype code as an example. Spend one hour together on day one walking through the structure.
Custom charts take longer than planned.	Use the fl_chart package first; exact animations can be polished in week 4.
Merge conflicts between branches.	One person per screen file; shared files (theme, common) change only through a pull request reviewed by Erwin.
Scope creep (real AI, login, camera).	Log it as phase 2. This month is the hardcoded version only, per the Features vs Budget board.

Out of scope this month

Login & accounts, database/backend, an AI Coach backed by an AI model, real camera and food recognition, Health Connect / HealthKit sync, scheduled notifications, and Play Store release.
